

Update on Construction Closeout of the Salesforce Transit Center


September 10, 2019



Contract Close out Status


Trade Group status:

- 22 Trade Groups in various stages of the Full & Final change order process
- 13 Trade Groups proceeding to Dispute Resolution
- 14 Trade Groups are closed out

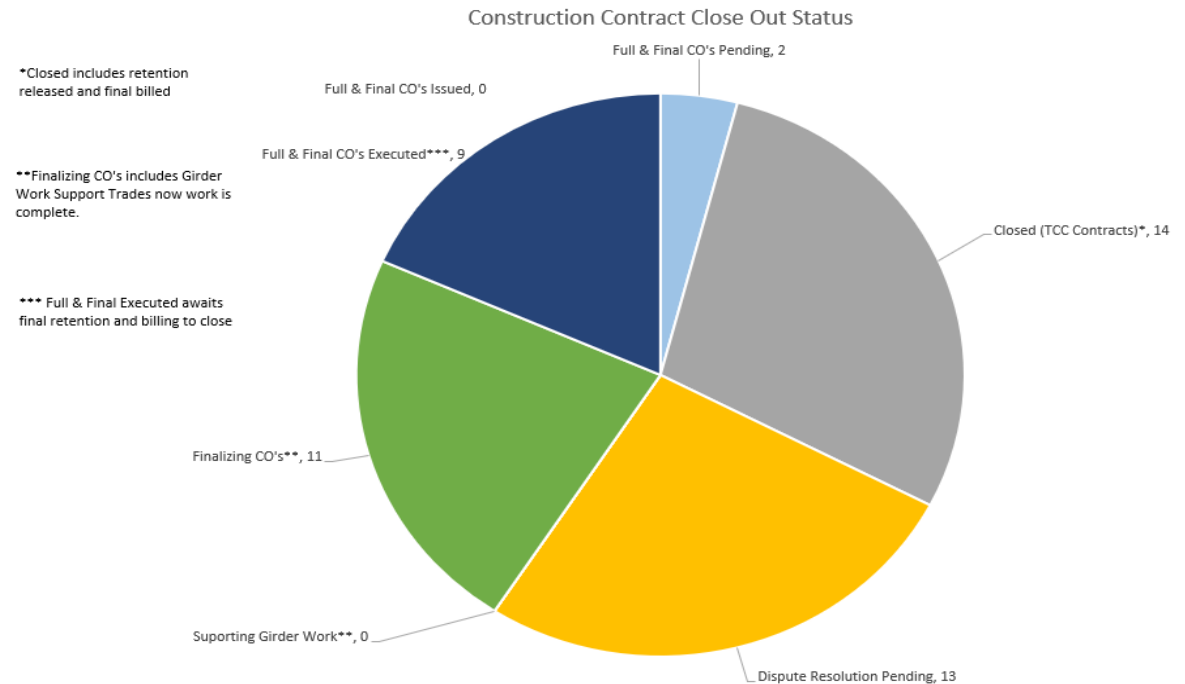

Contract Close out Status

Open Punch List Items per Trade Subcontractor

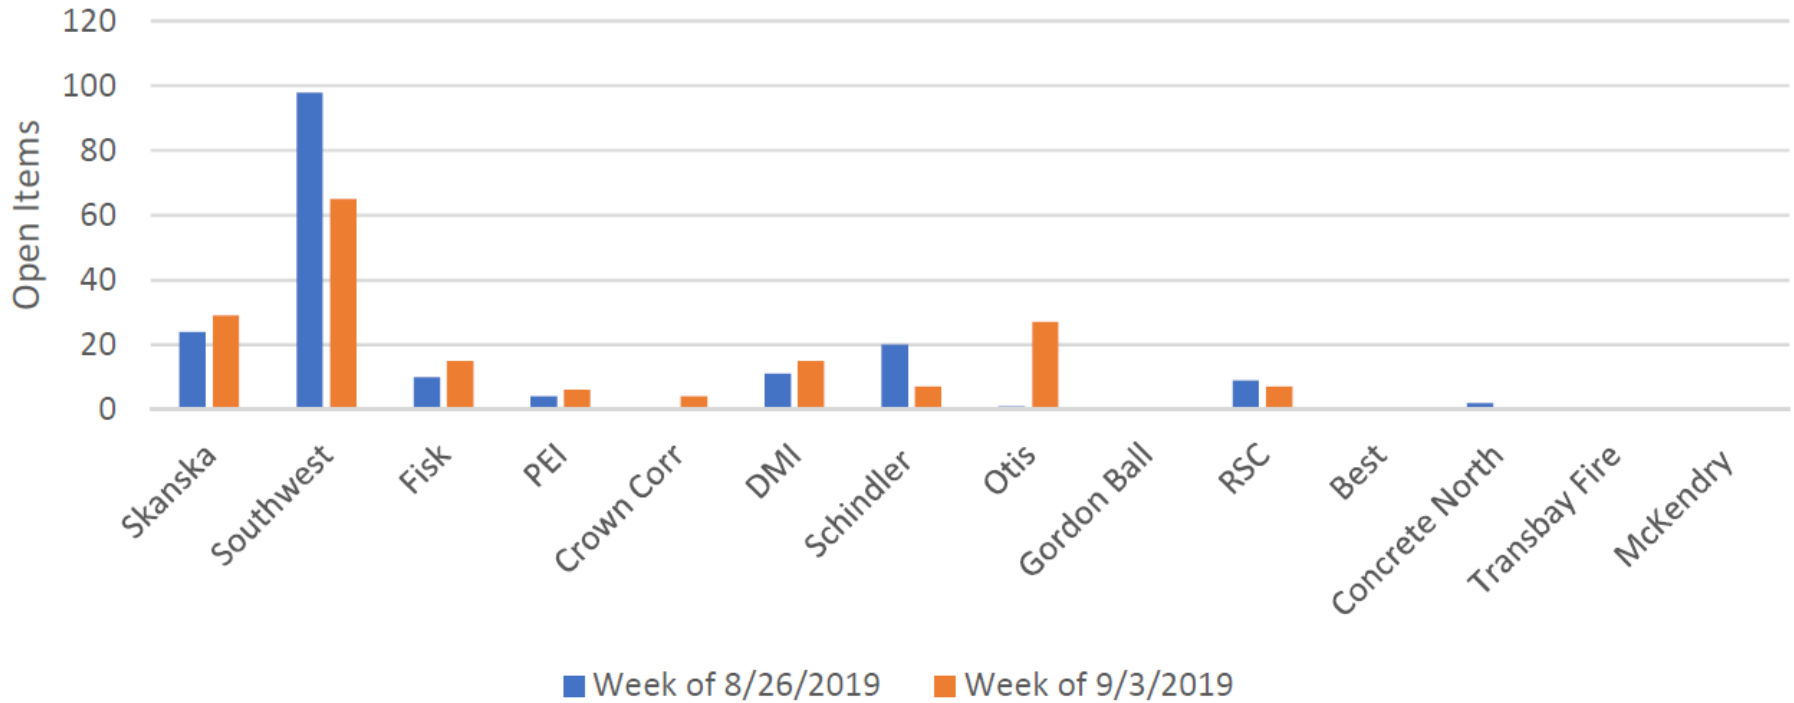

Contingency Tracking Cost (\$millions)

	Construction Contingency	CM/GC Contingency	Program Reserve	Total Contingency & Reserve
Baseline Budget Amounts	\$61.8	\$32.5	\$117.0	\$211.3
Contingency Usage Through July 2019	(\$54.4)	(\$26.2)	(\$86.8)	(\$167.4)
Remaining Baseline Budget Amounts (at July 2019)	7.4	6.3	30.2	\$43.9
Total Draws/Adds August 2019	(1.5)	(0.2)	0.0	(1.7)
Remaining Balances	\$5.9	\$6.1	\$30.2	\$42.2

Uses of Contingency this period

Extend plumbing lines to booths and gas meter room support and piping; Escalators, utility vaults & blockouts; Added support for Jenny Holzer art; and various other miscellaneous changes.

Forecasted Contingency Use

CM/GC: \$0.5M

Construction: \$1.5M

Program Reserve: \$0

Budget Status (\$millions)

	Current Budget	Expended thru 07/19*	Estimate at Completion
Construction	1,532.8	1,521.3	1,550.7
Construction and CM/GC Contingencies	12.0	-	-
Design and Support Contracts	621.8	611.3	623.8
Phase 1 Target	2,166.6	2,132.6	2,174.5
Tenant Improvements	35.5	10.5	35.5
301 Mission Legal	27.1	19.4	27.1
Phase 1 Target with TI and 301M Legal	2,229.2	2,162.5	2,237.1
Program Reserve	30.2	-	22.3
Total Phase 1 Program	2,259.4	2,162.5	2,259.4

* Some July actuals are estimated



Thank You

TJPA
TRANSBAY JOINT POWERS AUTHORITY

201 Mission Street, Suite 2100 San Francisco, CA 94105 • 415.597.4620 • www.tjpa.org
